ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Welhouse~Curtin Ave**	**60 days**	**Mon 6/17/24**	**Fri 9/6/24**	
2		Precon Meeting	0 days	0	0	
3		Project Start	1 day	Mon 6/17/24	Mon 6/17/24	
4		Traffic Control	1 day	Tue 6/18/24	Tue 6/18/24	3
5		Inlet Protection Maintance	1 day	Tue 6/18/24	Tue 6/18/24	4SS
6		Stump Removal Larger than 1", ground down 2" *Stumps marked with "X"	3 days	Tue 6/18/24	Thu 6/20/24	5SS
7		Full Depth Sawcut Concrete Pavement	1 day	Wed 6/19/24	Wed 6/19/24	6SS+1 day
8		Concrete Street Pavement Removal	5 days	Thu 6/20/24	Wed 6/26/24	7
9		Unclassified Excavation and EBS	8 days	Thu 6/27/24	Mon 7/8/24	8
10		8 Inch Road Base	5 days	Tue 7/9/24	Mon 7/15/24	9
11		Survey For Road Base	1 day	Tue 7/16/24	Tue 7/16/24	10
12		Set Line for Trimming and Lower Structures	2 days	Wed 7/17/24	Thu 7/18/24	11
13		Trimming and Joint Layout	2 days	Fri 7/19/24	Mon 7/22/24	12
14		Furnish and Install Sanitary Manhole Chimney Seal	2 days	Tue 7/23/24	Wed 7/24/24	13
15		Adjust Sanitary and Storm Manhole Castings	2 days	Thu 7/25/24	Fri 7/26/24	14
16		Adjust Inlet Casting	2 days	Mon 7/29/24	Tue 7/30/24	15
17		Adjust Water Valve Box	1 day	Wed 7/31/24	Wed 7/31/24	16
18		6" Concrete Integral Pavement West Side	4 days	Thu 8/1/24	Tue 8/6/24	17
19		Cure Time	3 days	Wed 8/7/24	Fri 8/9/24	18
20		6" Concrete Integral Pavement East Side	4 days	Mon 8/12/24	Thu 8/15/24	19
21		Cure Time	3 days	Fri 8/16/24	Tue 8/20/24	20
22		Adjoining Hand Pours and Curb/Gutter	9 days	Wed 8/21/24	Mon 9/2/24	21
23		Remove sidewalk and Place Base Course	5 days	Fri 8/16/24	Thu 8/22/24	20
24		Pour Sidewalk and and Driveway Aprons	8 days	Fri 8/23/24	Tue 9/3/24	23
25		3 Inch Pulverized Topsoild, Seed Mix #4 and E-Mat	3 days	Wed 9/4/24	Fri 9/6/24	24
26		Install Mainbox Provided by homeowner	1 day	Mon 9/9/24	Mon 9/9/24	25
27		Site walk through for cleanliness	0 days	Fri 9/6/24	Fri 9/6/24	25
28		Welhouse Complete	0 days	Fri 9/6/24	Fri 9/6/24	25
29		**Blue Development**	**60 days**	**Mon 7/8/24**	**Fri 9/27/24**	
30		Traffic Control	1 day	Mon 7/8/24	Mon 7/8/24	
31		Driveway Openings Marked	1 day	Tue 7/9/24	Tue 7/9/24	30
32		Full Depth Sawcut concrete pavement	1 day	Wed 7/10/24	Wed 7/10/24	31
33		Remove Existing 8" Concrete Street	2 days	Thu 7/11/24	Fri 7/12/24	32
34		Pour 30 Inch Curb and Gutter Wilson S	1 day	Mon 7/15/24	Mon 7/15/24	33
35		Survey For Roadway	3 days	Mon 7/15/24	Wed 7/17/24	33
36		Set Paving Line	4 days	Thu 7/18/24	Tue 7/23/24	35
37		Traimming/Joint Layout (EST 400Tons-Waste)	6 days	Wed 7/24/24	Wed 7/31/24	36
38		Furnish and Install Sanitary Manhole Chimney Seal	1 day	Thu 8/1/24	Thu 8/1/24	37
39		Adjust Inlet Casting	2 days	Fri 8/2/24	Mon 8/5/24	38
40		Adjust Water Valve Box	1 day	Tue 8/6/24	Tue 8/6/24	39
41		Adjust Sanitary and Storm Manhole Castings	1 day	Wed 8/7/24	Wed 8/7/24	40
42		Hand Pour Terra Blue Ct/Tanah Trail (Culdesac) 8" Reinforced	5 days	Thu 8/8/24	Wed 8/14/24	41
43		8" Concrete Street Patching Wilson St	1 day	Thu 8/8/24	Thu 8/8/24	41
44		Cure Time Wilson St (Patches)	3 days	Fri 8/9/24	Tue 8/13/24	43
45		Mainine Paving Terra Blue Ct 8" Reinforced to Wilson St	7 days	Thu 8/15/24	Fri 8/23/24	42
46		Cure Time Terra Blue	3 days	Mon 8/26/24	Wed 8/28/24	45
47		Hand Pour Tanah Trail (RD) 6" Concrete	2 days	Thu 8/29/24	Fri 8/30/24	46
48		Mainline Paving Satori Trail From Tera Blue To Wilson St 6" Concrete	7 days	Mon 9/2/24	Tue 9/10/24	47
49		Cure time Satori Trail	3 days	Wed 9/11/24	Fri 9/13/24	48
50		Pave Wilson St 8" Reinforced	4 days	Mon 9/16/24	Thu 9/19/24	49
51		Cure Time Wilson St	3 days	Fri 9/20/24	Tue 9/24/24	50
52		Papermill Run Asphalt Transition	1 day	Wed 9/25/24	Wed 9/25/24	51
53		1- Foot Thick Fravel Driveway Pad	3 days	Wed 9/25/24	Fri 9/27/24	51
54		12" Thick Gravel -Tanah Trail/Blue CT Culdesac Islands	1 day	Wed 9/25/24	Wed 9/25/24	51
55		Terrance Backfilling (Estimated 1,100 CY.)	1 day	Thu 9/26/24	Thu 9/26/24	54
56		Terrace Temporay Seeding/Mulching (Estimated 3,500 S.Y.)	1 day	Fri 9/27/24	Fri 9/27/24	55
57		Site walk through for Cleanliness	0 days	Fri 9/27/24	Fri 9/27/24	56
58		Blue Dev Complete	0 days	Fri 9/27/24	Fri 9/27/24	56
59		**RailRoad St**	**60 days**	**Mon 6/17/24**	**Fri 9/6/24**	
60		Traffic Control	1 day	Thu 8/8/24	Thu 8/8/24	41
61		Full Depth Sawcut Concrete Pavement	1 day	Fri 8/9/24	Fri 8/9/24	60
62		Remove Existing Concrete Pavement/(	1 day	Mon 8/12/24	Mon 8/12/24	61
63		Tie bar Placement Dilled/Set	1 day	Tue 8/13/24	Tue 8/13/24	62
64		Hand Pour, Concrete Pavement/Curb/S	1 day	Wed 8/14/24	Wed 8/14/24	63
65		Cure time	3 days	Thu 8/15/24	Mon 8/19/24	64
66		Site Walk Through for Cleanliness	0 days	Mon 8/19/24	Mon 8/19/24	65
67		RailRoad Complete	0 days	Mon 8/19/24	Mon 8/19/24	65

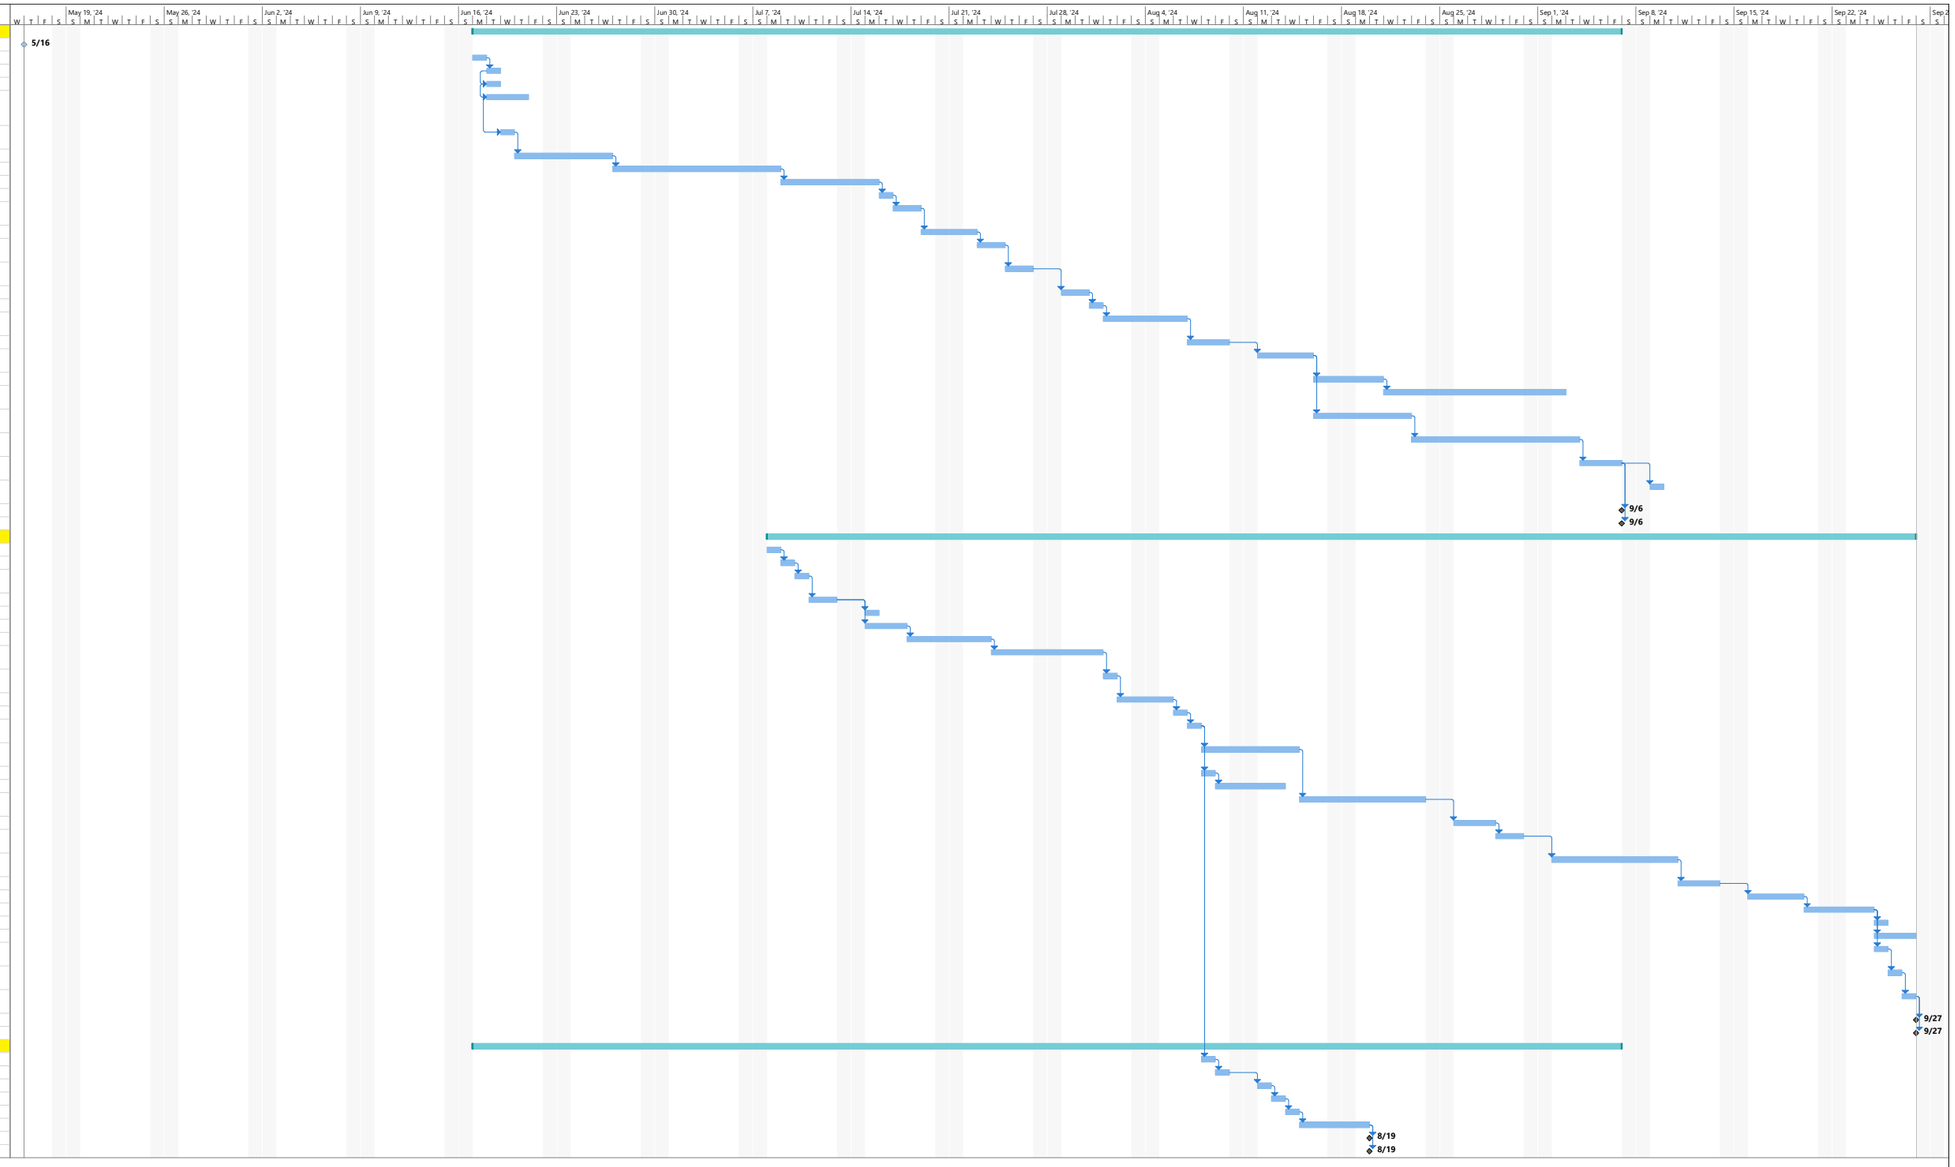

Project: Project1
Date: Thu 5/16/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
